

Foothill College Site Improvements

Foothill – De Anza Community College District

Board of Trustees Presentation

May 7, 2012



FOOTHILL COLLEGE

PRESENTATION OVERVIEW

- Campus Outreach Efforts
- Project Timeline & Construction Phasing
 - #162 Parking & Circulation
 - Phase 1 Summer 2012
 - Phase 2 Summer 2013
 - #144 Central Campus Site Improvements
 - Summer & Fall 2012
- Mitigation of Construction Impacts with emphasis maintaining enrollment



PROJECT TEAM & **OUTREACH EFFORTS**

Steering Committee

Frank Nunez (FHDA)
Art Heinrich (FHDA)
Shirley Treanor (Foothill)
Brenda Visas (Foothill)
Annette Stenger (Foothill)
Chief Ron Levine (Police)
Todd Leicht (Gilbane / Maas)

Project Design Team

WRNS Studio (Wright Sherman)
Meyer Silberberg Land Architects
SANDIS, Civil Engineers
Fehr & Peers, Traffic Engineers
Silverman & Light
Crosby Group , Structural Engineers



Campus Outreach

Sustainability Committee
Building & Grounds
Academic Senate
Administration Council
Classified Senate
Planning & Resource Committee (PaRC)
President' s Cabinet
Associated Student Body (soon)
Central Services (soon)

Technical Outreach

Traffic Studies
VTA
District Police

CONSTRUCTION PROCESS

GUIDING PRINCIPLES

- Maintain student enrollment
- Limit impact on educational offerings
- Student safety
- Maintain accessibility and circulation
- Convenience
- Sustainability
- Apply engineering best practices

GOALS

- Safety Improvements: Vehicle, pedestrian, bicycle
- Enhance and improve accessibility
- Limit impact on parking
- Aesthetics – maintain beauty of campus
- Lighting improvements and signage
- Reduce traffic congestion & improve efficiency
- Protect, renew, and enhance the integrity of the campus
- Improve storm-water management




EXPECTATIONS FOR SUMMER & FALL 2012

SUMMER 2012:

- Extensive Construction Throughout Central and Outer Campus
- PSEC Bus Stop Closed

FALL 2012:

- Irrigation and Planting will continue
- Northern Threshold and Stairs under Construction
- New Pathways will be Accessible, Safe, Barrier Free
- Improved Pathway Lighting
- Fountains Restored

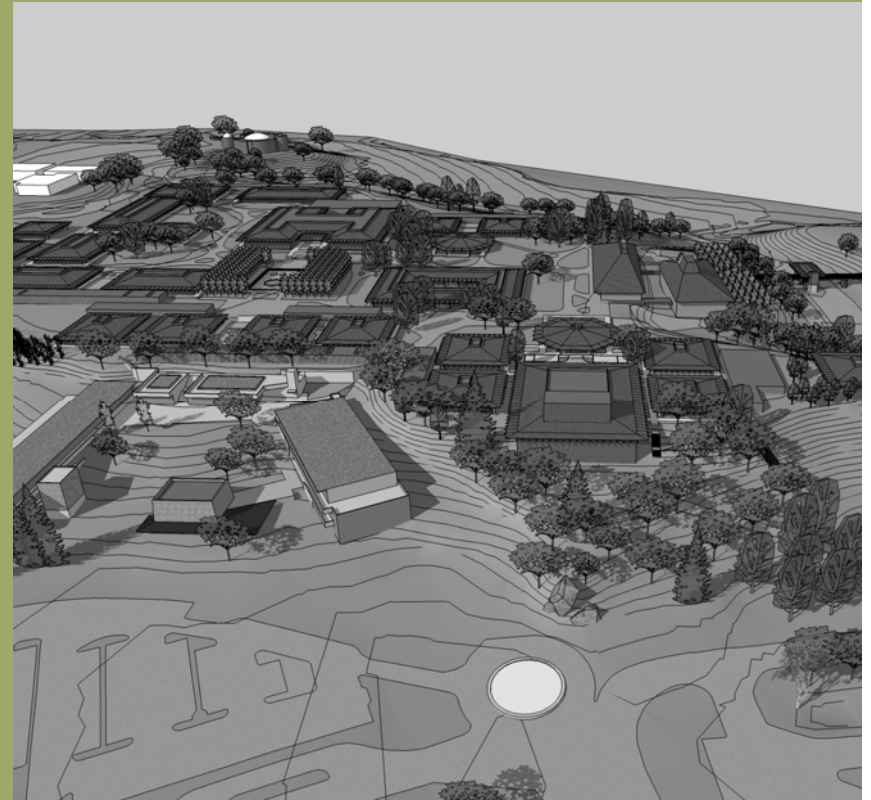

LESSONS LEARNED & BEST PRACTICES

De Anza Combined Site Improvements Phase I Foothill Utilities Infrastructure Project Phase I

- **Minimize impact on enrollments**
- **Minimize impact on parking**
- **Clearly defined paths for travel (signage)**
- **Utilize proven Campus Notification Protocols**
 - **Steering Committee**
 - **Foothill Fusion Newsletter**
 - **Measure C Construction Web Page**
- **Collaborative Scheduling with Contractor and College**


MITIGATION OF CONSTRUCTION IMPACTS

- **Coordinate Construction with Academic Calendar**
- **Maintain Accessible Routes**
- **Emergency Vehicle Access**
- **Comprehensive Signage Plan**



Project #162 – Parking & Circulation


**Phase 1
2012**

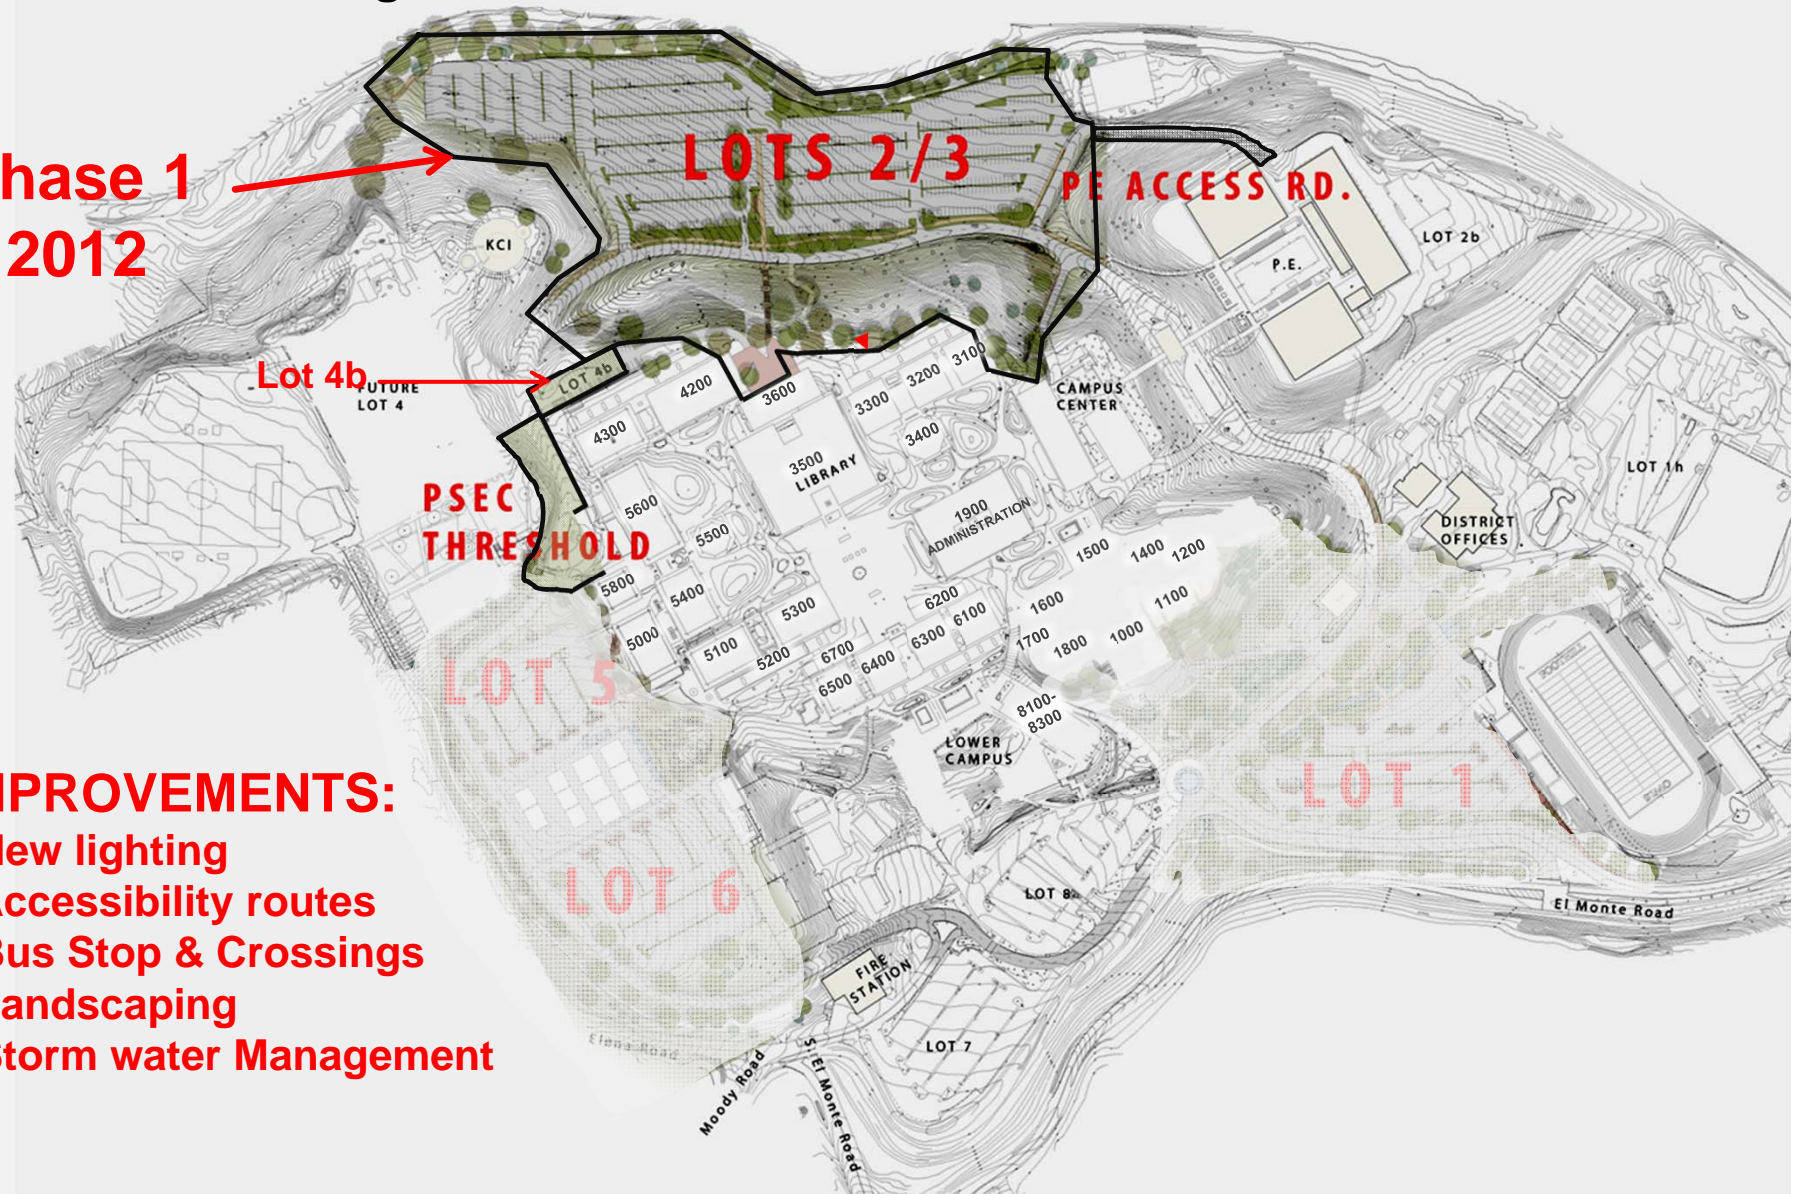

IMPROVEMENTS:

- New lighting
- Accessibility routes
- Bus Stop & Crossings
- Landscaping
- Storm water Management


Project #162 – Parking & Circulation

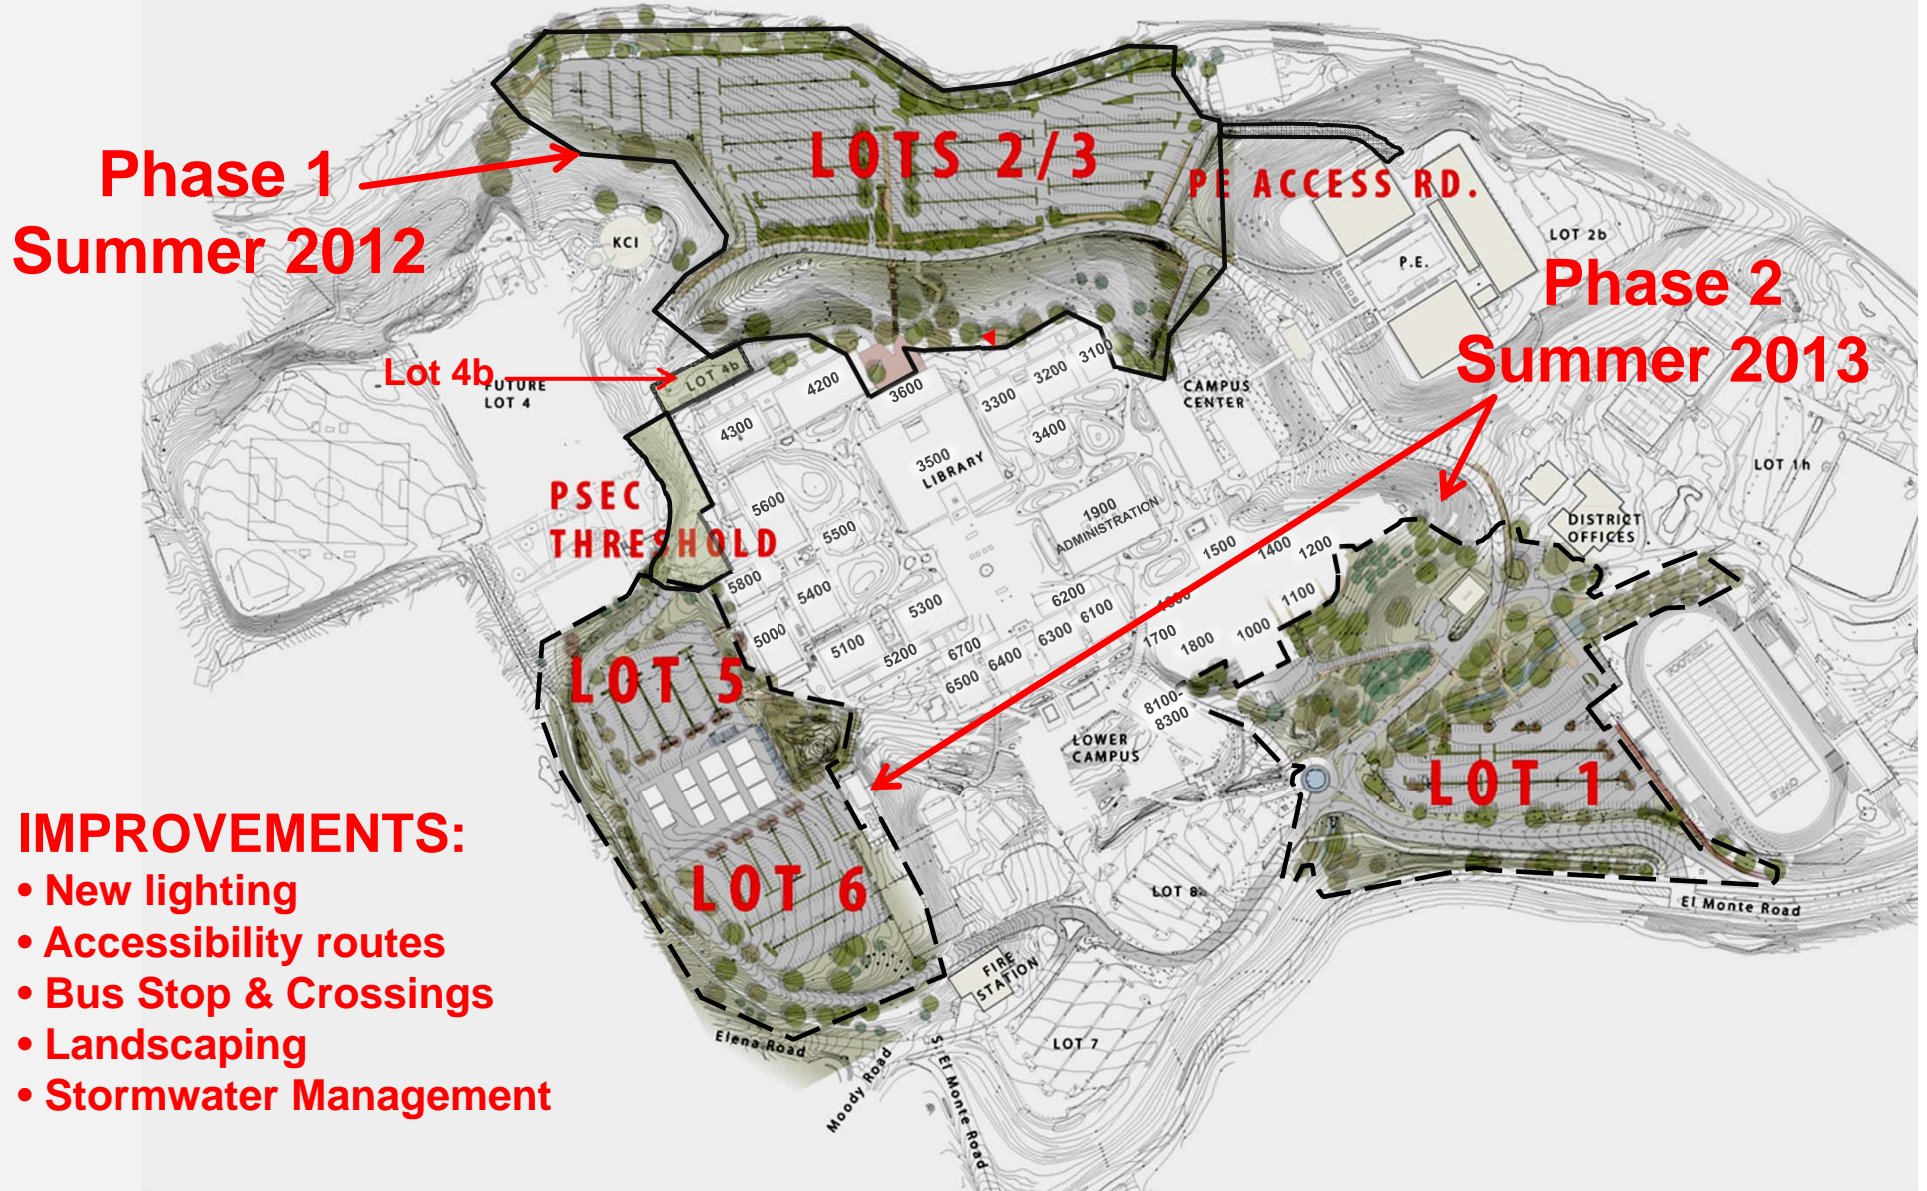

IMPROVEMENTS:

- New lighting
- Accessibility routes
- Bus Stop & Crossings
- Landscaping
- Stormwater Management


Project #162 – Parking & Circulation

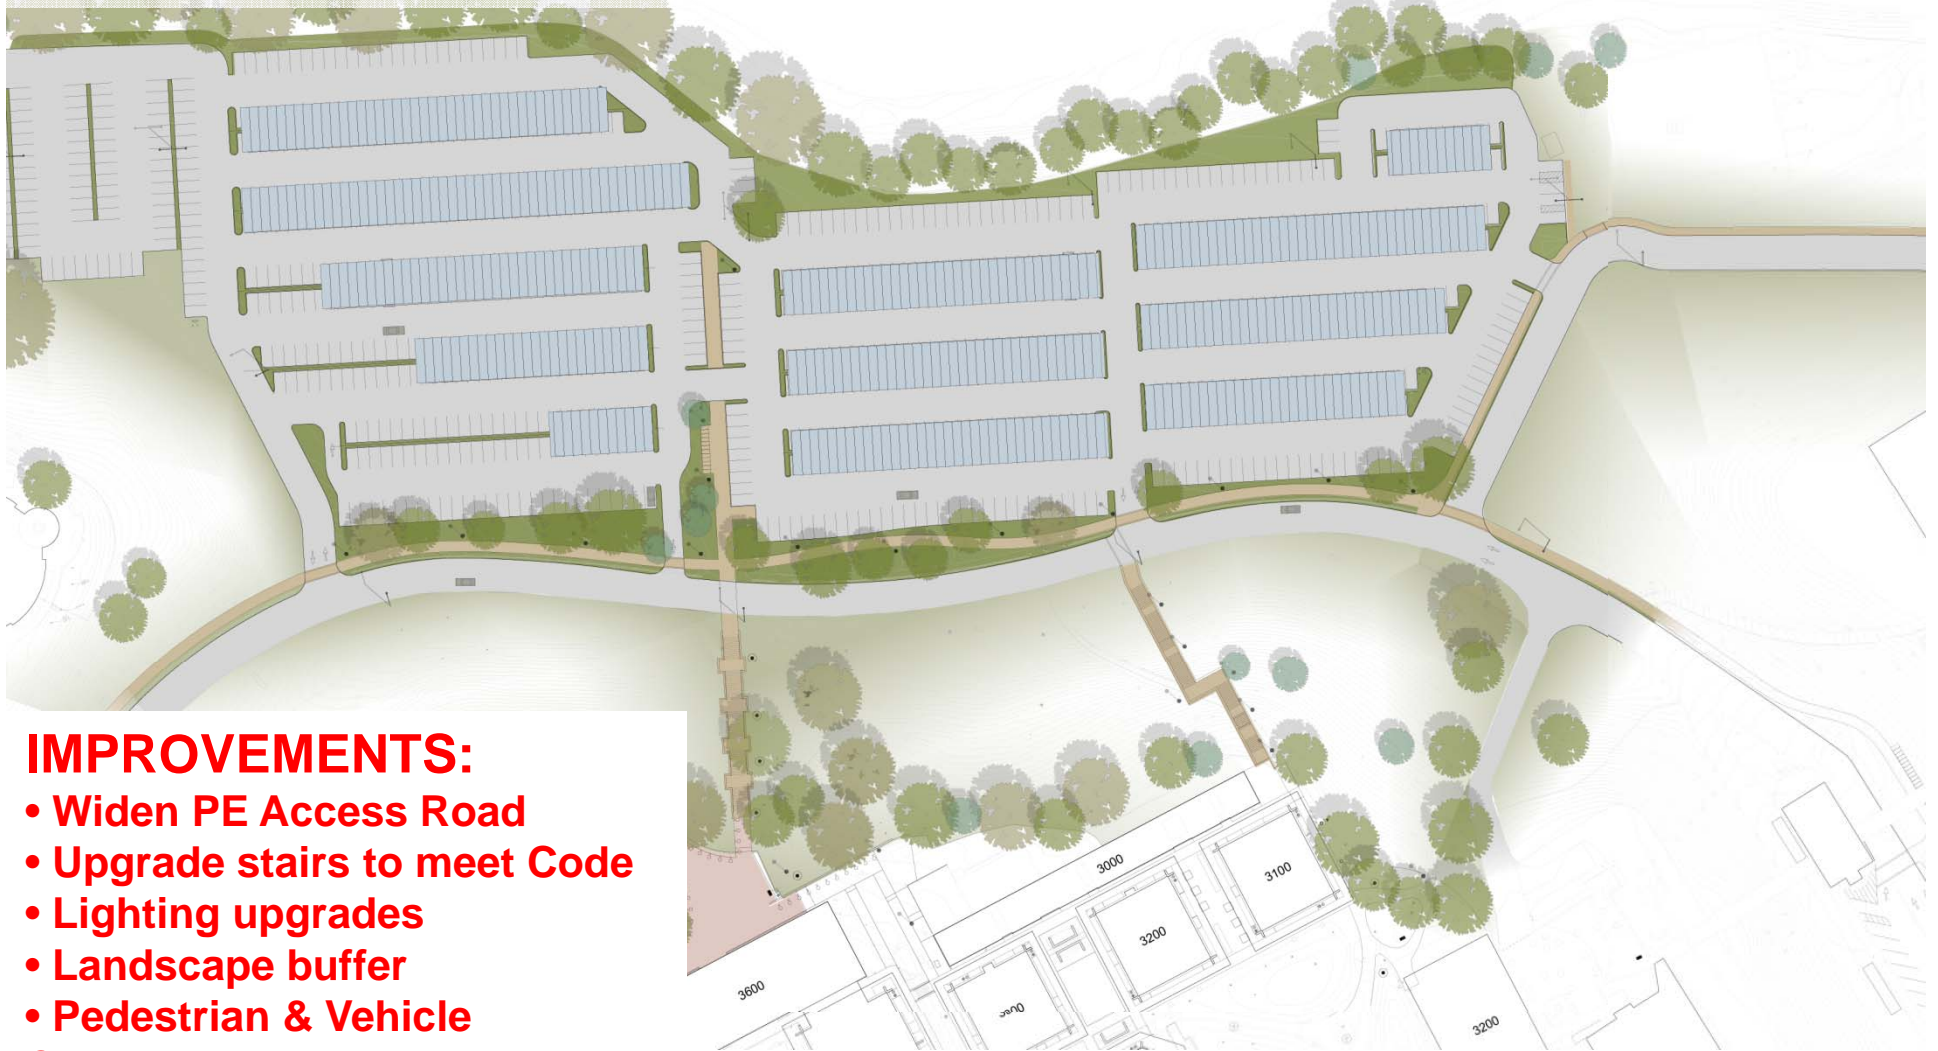

IMPROVEMENTS:

- Widen PE Access Road
- Upgrade stairs to meet Code
- Lighting upgrades
- Landscape buffer
- Pedestrian & Vehicle Circulation
- Stormwater Management


Project #162 – Parking & Circulation

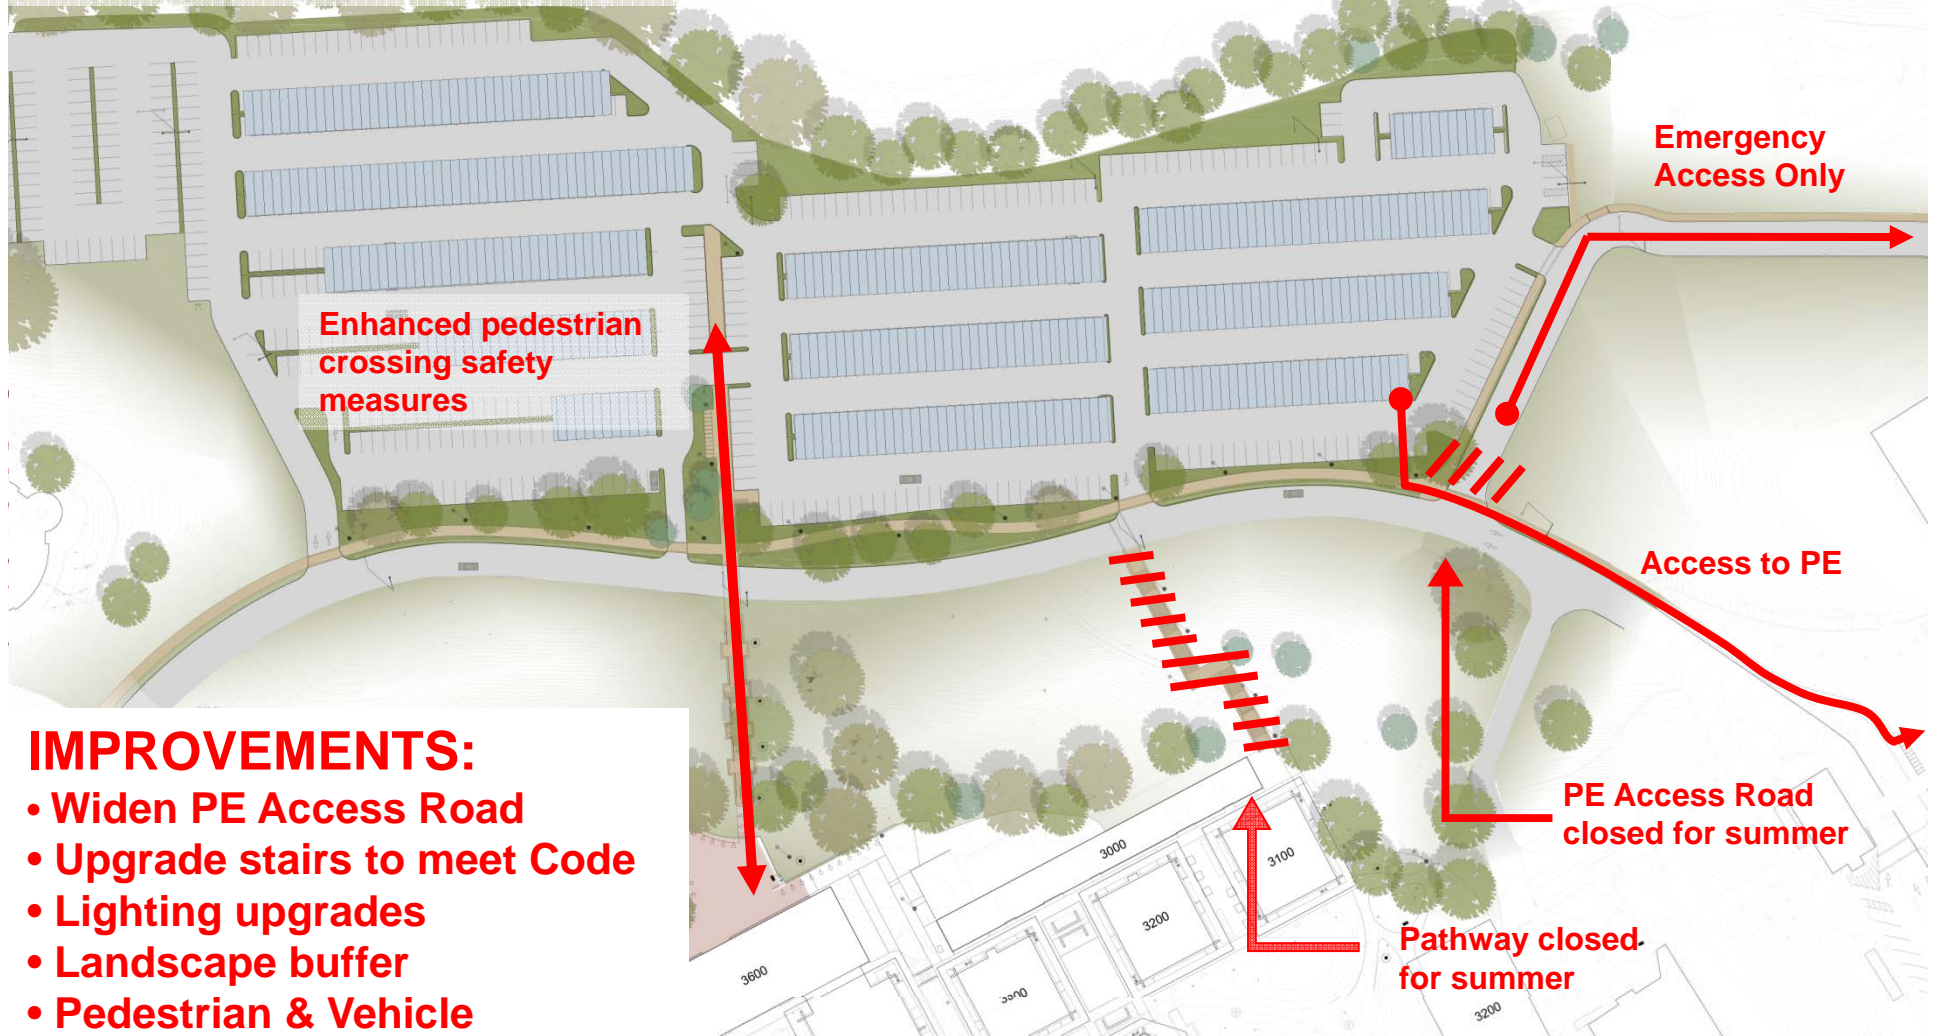

IMPROVEMENTS:

- Widen PE Access Road
- Upgrade stairs to meet Code
- Lighting upgrades
- Landscape buffer
- Pedestrian & Vehicle Circulation
- Stormwater Management


Project #162 – Parking & Circulation

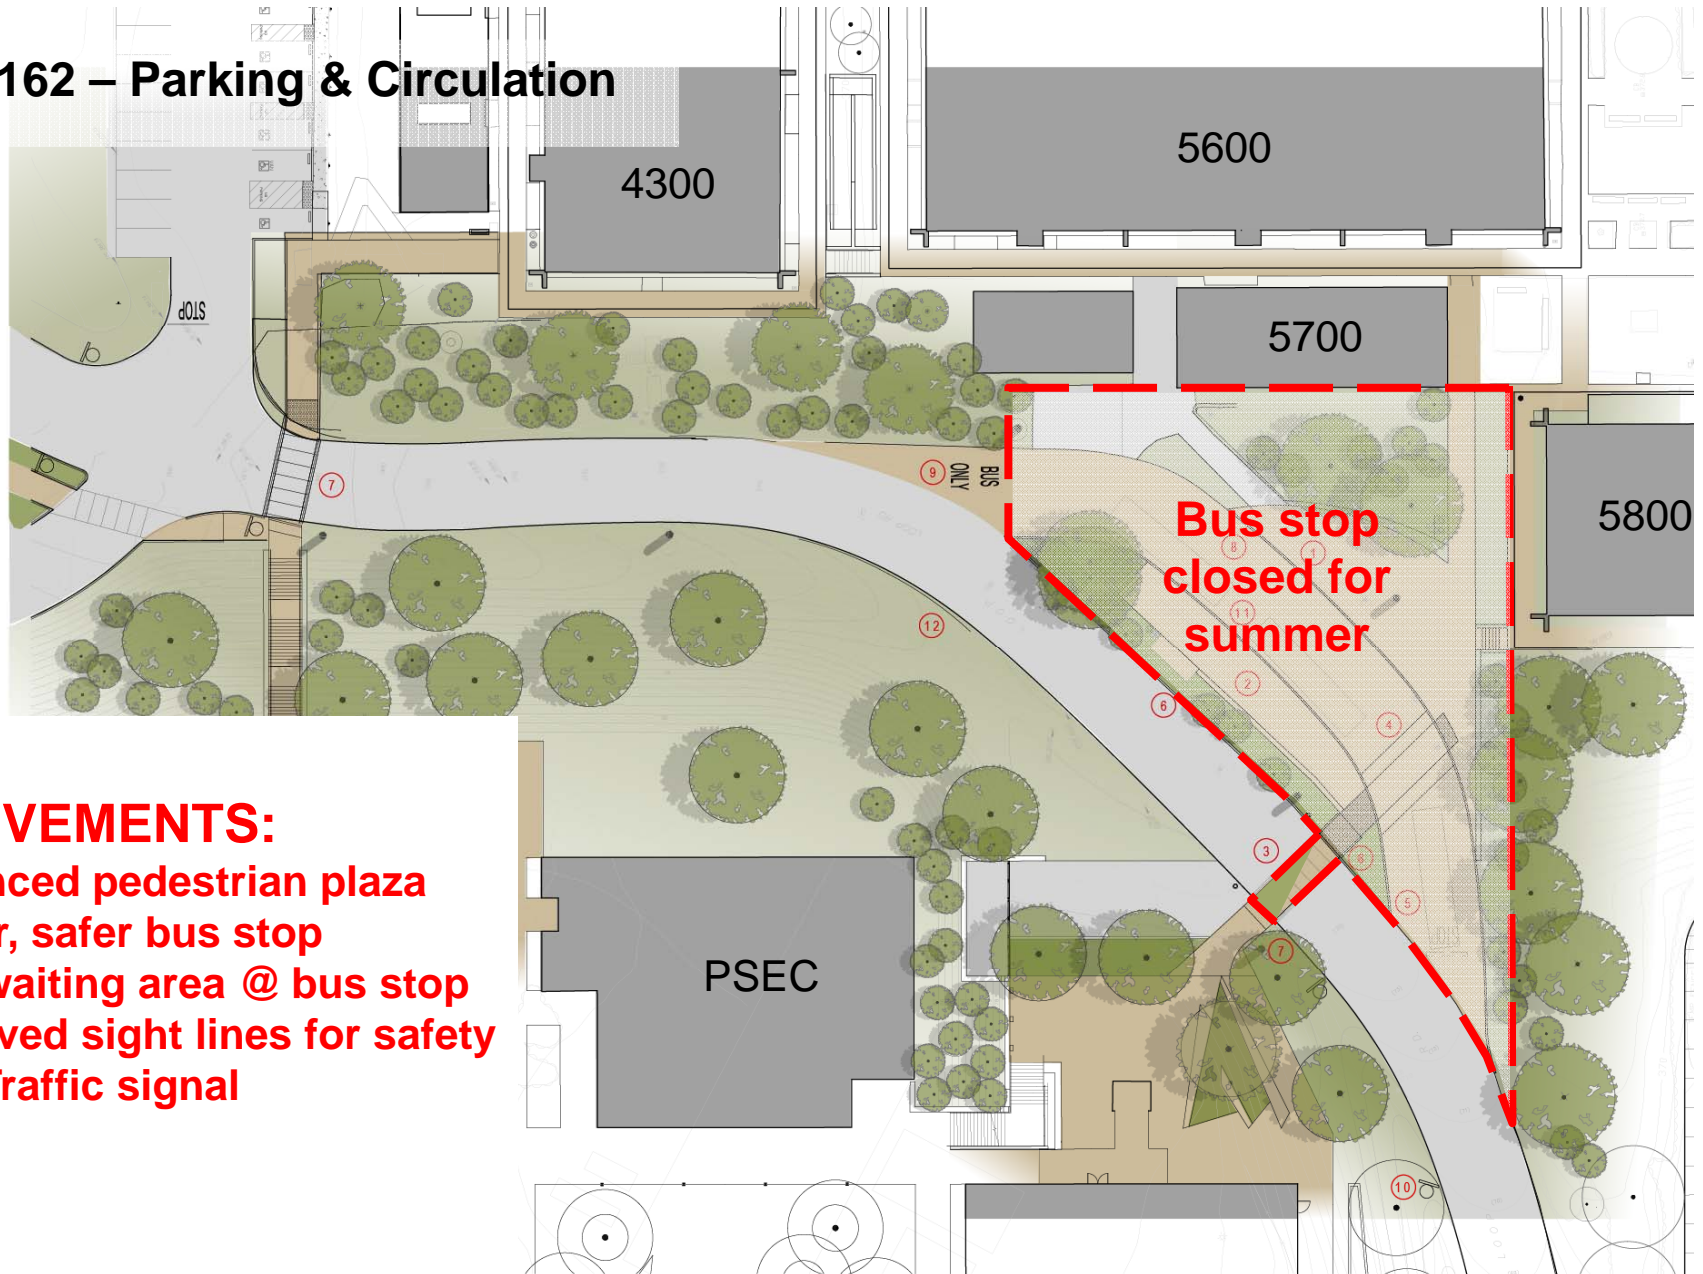

IMPROVEMENTS:

- Enhanced pedestrian plaza
- Larger, safer bus stop
- Safe waiting area @ bus stop
- Improved sight lines for safety
- New Traffic signal


Project #144 – Central Campus Site Improvements

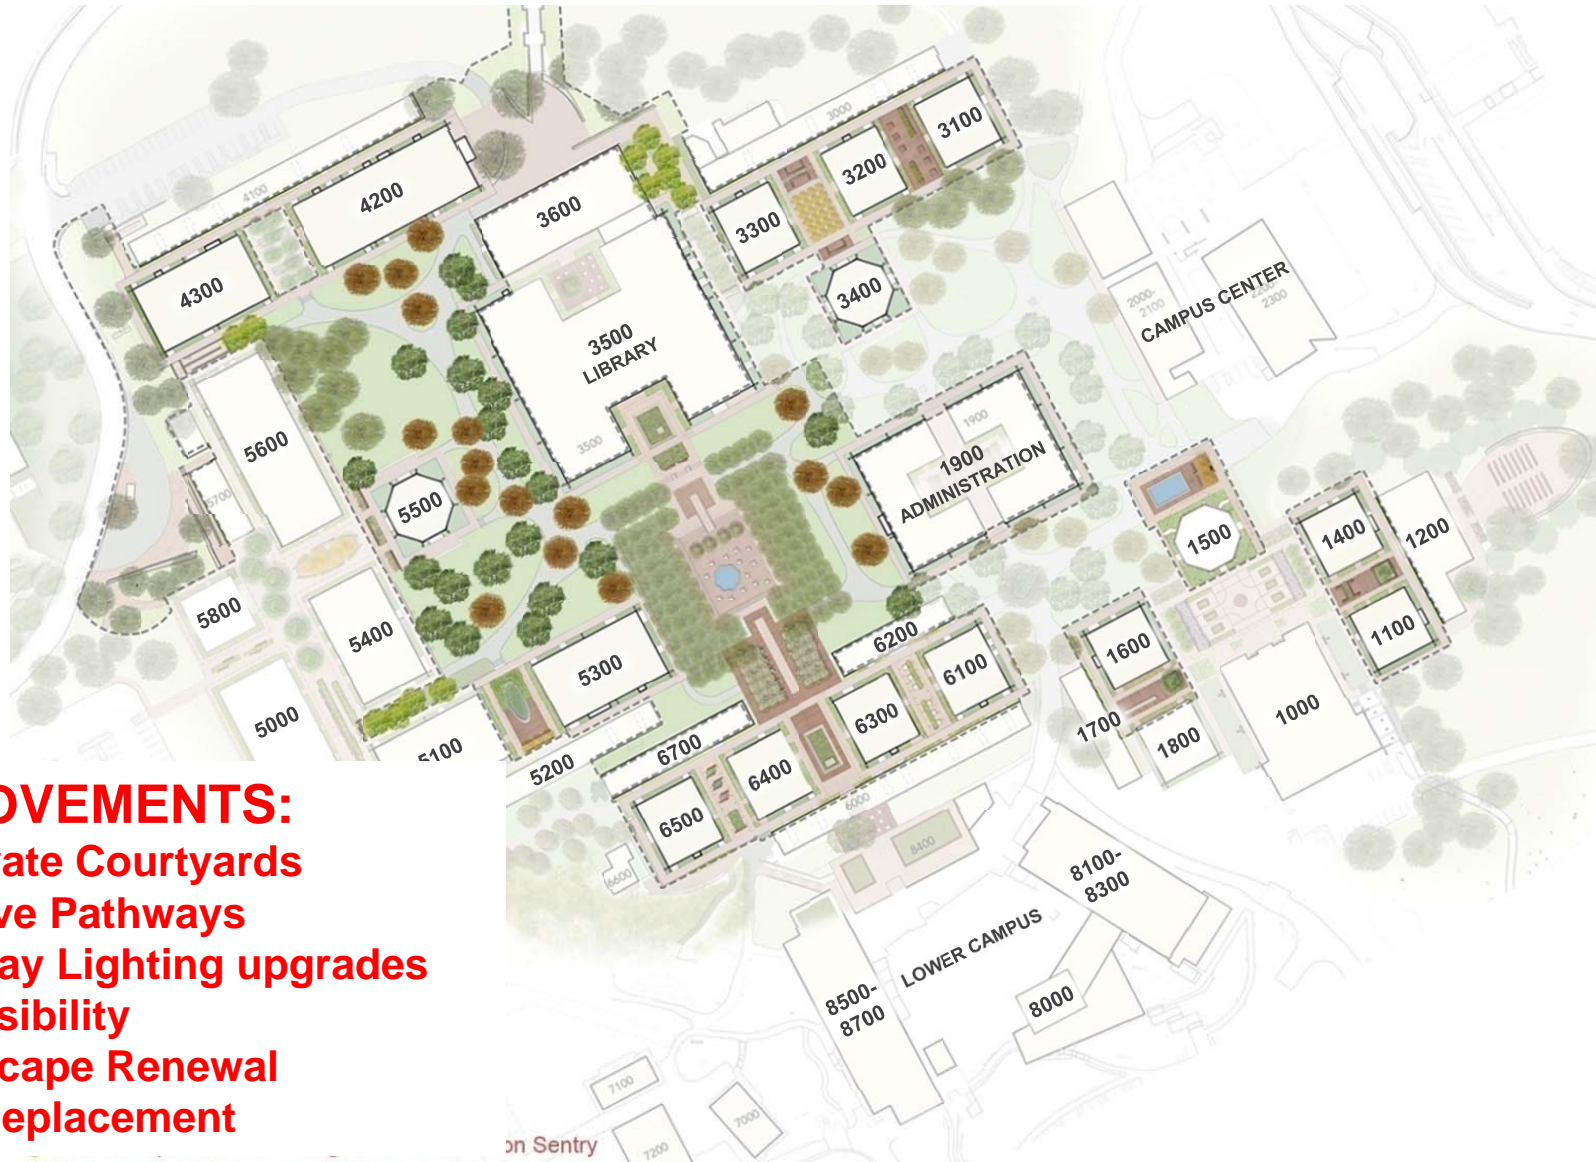

IMPROVEMENTS:

- Renovate Courtyards
- Improve Pathways
- Pathway Lighting upgrades
- Accessibility
- Landscape Renewal
- Tree Replacement

Project #144 – Central Campus Construction Mitigation & Accessibility

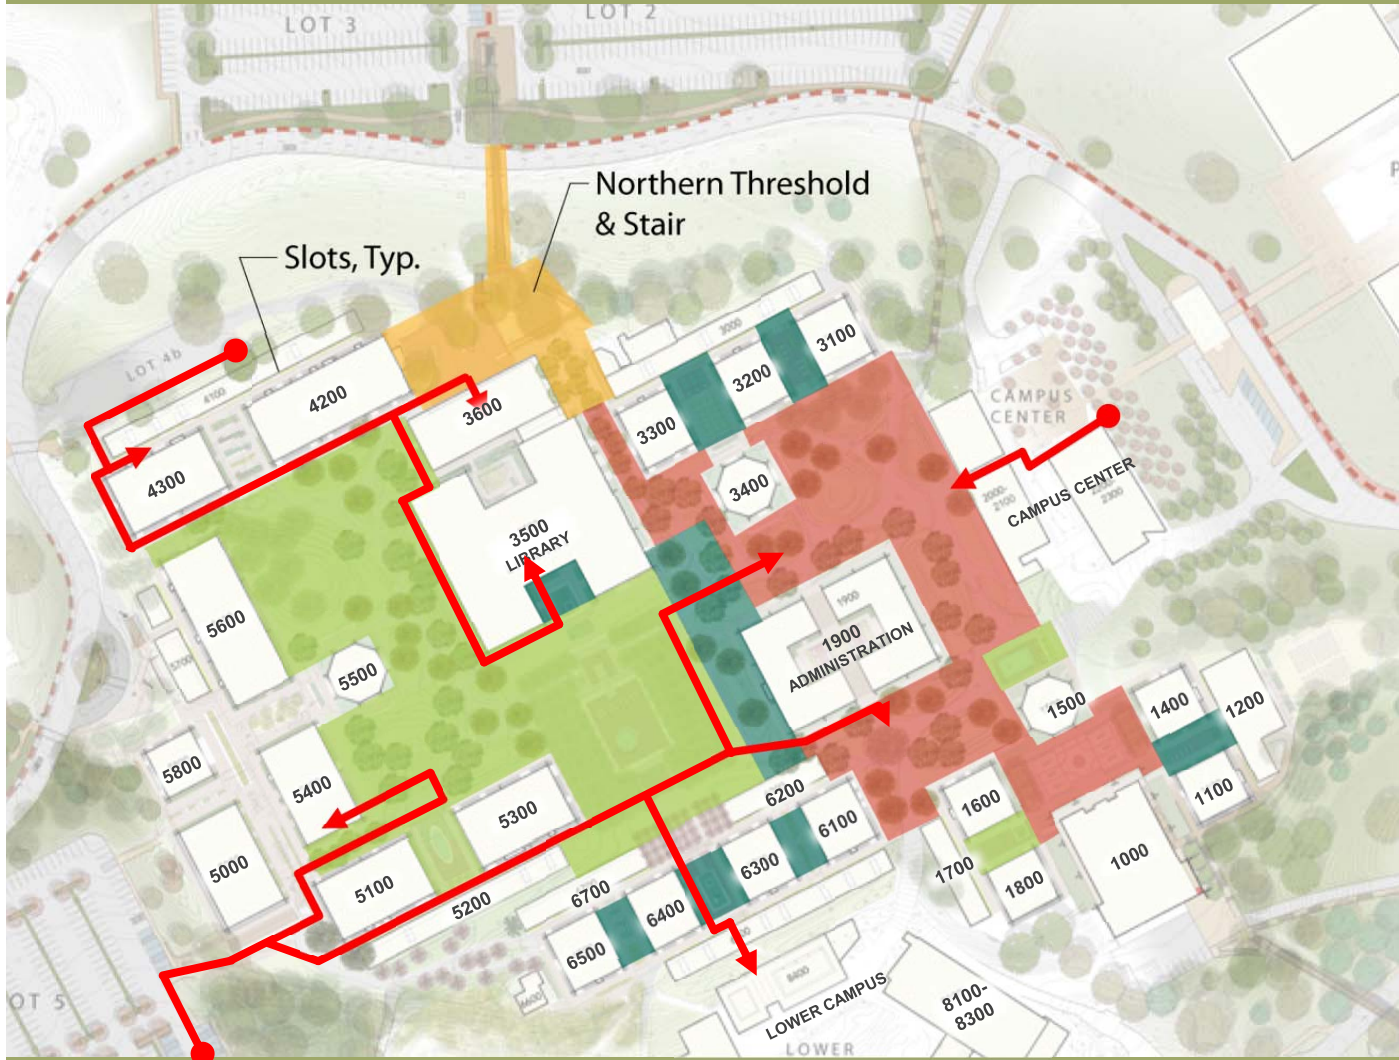

2012 CONSTRUCTION

	Area 1	JULY – SEPT
	Area 2	AUG – SEPT
	Area 3	JULY – SEPT
	Area 4	OCT – DEC

Project #144 - Central Campus Tree Replacement



Project #144 - Central Campus Tree Replacement



Foothill College Site Improvements

Foothill – De Anza Community College District

Board of Trustees Presentation

May 7, 2012



FOOTHILL COLLEGE
